

MONTHLY PROGRESS REPORT OF “AKANKSHA PROJECT” AT NEW TOWN AS STOOD ON 15/07/2020

Sl No	Name of The Work	Name of The Agency	Estimated Amount (Rs.)	Tender Amount (Rs.)	Date of Commencement	Date Of Completion	Cumulative Physical Progress Achieved (Civil)	Financial Progress (Civ+Ele)	Balance Work
1	Construction of 3 (Three) nos B type (Classic) G+10 storied Residential Building including Structural, Sanitary and Plumbing and Electrical works under AKANKHA Scheme at Rajarhat Action Area - 1D during the year 2015-16. (Tender NO:- 12 of 2016-17 of SE/S.C, Housing Directorate)	Mackintosh Burn Limited	52,24,32,813.00	46,92,49,152.00	01/12/2016	31/08/2020	95.00%	92.00 %	<p><u>Marble Floor& Kota Stone At Lobby :-</u> <u>Classic-1:-</u> completed except final cut <u>Classic-2:-</u> completed except final cut . <u>Classic-3:-</u> completed except final cut</p> <p><u>. Aluminum work at Lobby</u> <u>Classic-1:-</u> 35% completed <u>Classic-2:-</u> not started <u>Classic-3:-</u> 25% completed</p> <p><u>Flush Door Polishing & Panel shutter Painting</u> <u>Classic-1:-</u> 1st floor to 10 thfloor single coat painting completed <u>Classic-2:-</u> 1st floor to 10 thfloor single coat painting completed <u>Classic-3:-</u> 1st floor to 10 thfloor single coat painting completed</p> <p><u>External Painting</u> <u>Classic-1:-</u> Completed except Stair room Painting work and Ground floor Painting work <u>Classic-2:-</u> Completed except Stair room Painting work and Ground floor Painting work <u>Classic-3:-</u> Completed except Stair room Painting work and Ground floor Painting work</p> <p><u>Lobby Portion Colour Painting</u> <u>Classic-1:-</u> 1st floor to 3rd floor single coat completed <u>Classic-2:-</u> not started <u>Classic-3:-</u> 1st floor to 3rd floor single coat completed</p> <p><u>Grill & Collapsible gate Painting Work</u> <u>Classic-1:-</u> 50% completed <u>Classic-2:-</u> 50% completed <u>Classic-3:-</u> 25% completed</p>

MONTHLY PROGRESS REPORT OF “AKANKSHA PROJECT” AT NEW TOWN AS STOOD ON 15/07/2020

Sl No	Name of The Work	Name of The Agency	Estimated Amount (Rs.)	Tender Amount (Rs.)	Date of Commencement	Date Of Completion	Physical Progress (Civil)	Cumulative Physical Progress Achieved (Civil)	Financial Progress (Civ+Ele)	Remarks
2	Construction of 3 (Three) nos (G+10) Storied A1 Type (Premium), One no (G+10) Storied A2 Type (Elegant) Residential Building, Community Hall and Substation Building [2 nos.] including Main Sewer Line, Under Ground water Supply System, Rainwater Harvesting pit, Rain water Recharge pit [3 Nos.], Horticulture & Bituminous Road under AKANKSHA Scheme at Rajarhat, New Town Action area-1D during the year 2015-16: Structural, S & P, Electrical and Roads works. (Tender No:-18 of 2016-17 of the S.E/S.C,Housing Directorate)	Delta Construction	73,44,71,942.00	61,83,51,928.00	16/01/2017	31/08/2020	5.00 %	98.00%	90.00 %	<p><u>Marble Floor& Kota Stone At Lobby :-</u> <u>PR 1:-</u> completed except Ground floor <u>PR-2:-</u> completed except Ground floor. <u>PR-3:-</u> completed except Ground floor Elegant; completed except Ground floor</p> <p><u>Flush Door Polishing & Panel shutter Painting</u> <u>PR 1:-</u> completed except 1st & 2nd floor <u>PR-2:-</u> completed except. 1st & 2nd floor <u>PR-3:-</u> completed except 1st & 2nd floor Elegant: started</p> <p><u>External Painting</u> <u>PR 1:-</u> completed except Ground floor <u>PR-2:-</u> completed except Ground floor. <u>PR-3:-</u> completed except Ground floor Elegant; completed except Ground floor</p> <p><u>Lobby Portion Colour Painting</u> <u>PR 1:-</u> completed except 1st floor <u>PR-2:-</u> completed except 1st floor. <u>PR-3:-</u> completed except 1st floor Elegant: started</p> <p><u>Grill & Collapsible gate Painting Work</u> <u>PR 1:-</u> completed except 1st & 2nd floor <u>PR-2:-</u> completed except 1st & 2nd floor <u>PR-3:-</u> completed except 1st floor Elegant: completed except 1s t to 3rd floor</p>

MONTHLY PROGRESS REPORT OF “AKANKSHA PROJECT” AT NEW TOWN AS STOOD ON 15/07/2020

Sl No	Name of The Work	Name of The Agency	Estimated Amount (Rs.)	Tender Amount (Rs.)	Date of Commencement	Date Of Completion	Cumulative Physical Progress Achieved	Financial Progress	Remarks
1	” Construction of 3 (Three) nos (G+10) Storied A1 Type (Premium), One no (G+10) Storied A2 Type (Elegant) Residential Building, Community Hall and Substation Building [2 nos.] including Main Sewer Line, Under Ground water Supply System, Rainwater Harvesting pit, Rain water Recharge pit [Three Nos.], Horticulture & Bituminous Road under AKANKSHA Scheme at Rajarhat, New Town Action area-1D during the year 2015-16: structural, S & P, Electrical and Roads works"— Balance Work(Extension of Tender No-18 A of 2016-17 of SE/SC, H.Dte.	Delta Construction	19,23,18,504.00	16,19,12,949.00	15/03/2019	31/08/2020	65 %	50 %	<p>1. UnderGround Reservoir Waterproofing, Internal plastering and Manhole cover work pending</p> <p>2. Community Hall:- Brick work 70% completed. Internal plaster 50% completed</p> <p>3. Cable Trench :- 90% completed</p> <p>4. Road Work 70% completed</p> <p>5. Sewer line & Inspection Pit 90% completed</p> <p>6. Drinking water line 70% completed</p>

MONTHLY PROGRESS REPORT OF "AKANKSHA PROJECT" AT NEW TOWN AS STOOD ON 15/07/2020

Sl No	Name of The Work	Name of The Agency	Estimated Amount (Rs.)	Tender Amount (Rs.)	Date of Commencement	Date Of Completion	Cumulative Physical Progress Achieved	Financial Progress	Remarks
1	Construction of boundary wall for Akanksha Project at New Town	S.S. Enterprise	97,59,234.00	96,12,845.00	16/01/2019	31/12/2019	80.00 %	60.00 %	Priming & Painting Work, Finshing work Of Security Room,Entrance Gate work in progress

MONTHLY PROGRESS REPORT OF “AKANKSHA PROJECT” AT NEW TOWN AS STOOD ON 15/07/2020

Sl No	Name of The Work	Name of The Agency	Estimated Amount (Rs.)	Tender Amount (Rs.)	Date of Commencement	Date Of Completion	Cumulative Physical Progress Achieved	Financial Progress	Remarks
1	Sewerage Treatment plant(S.T.P) of capacity 420 m ³ /day for Akanksha Project at New Town, Rajarhat at Plot DB-2, Action Area-ID(Civil Work)	Master Construction	1,24,52,822.00	1,22,51,086.00	12/02/2019	31/08/2020	96.00 %	75.00 %	External & Internal Painting work balance.



REDMI NOTE 8
AI QUAD CAMERA

PREMIUM & ELEGANT



PREMIUM & ELEGANT



PREMIUM & ELEGANT




PREMIUM & ELEGANT



REDMI NOTE 8
AI QUAD CAMERA

PREMIUM & ELEGANT

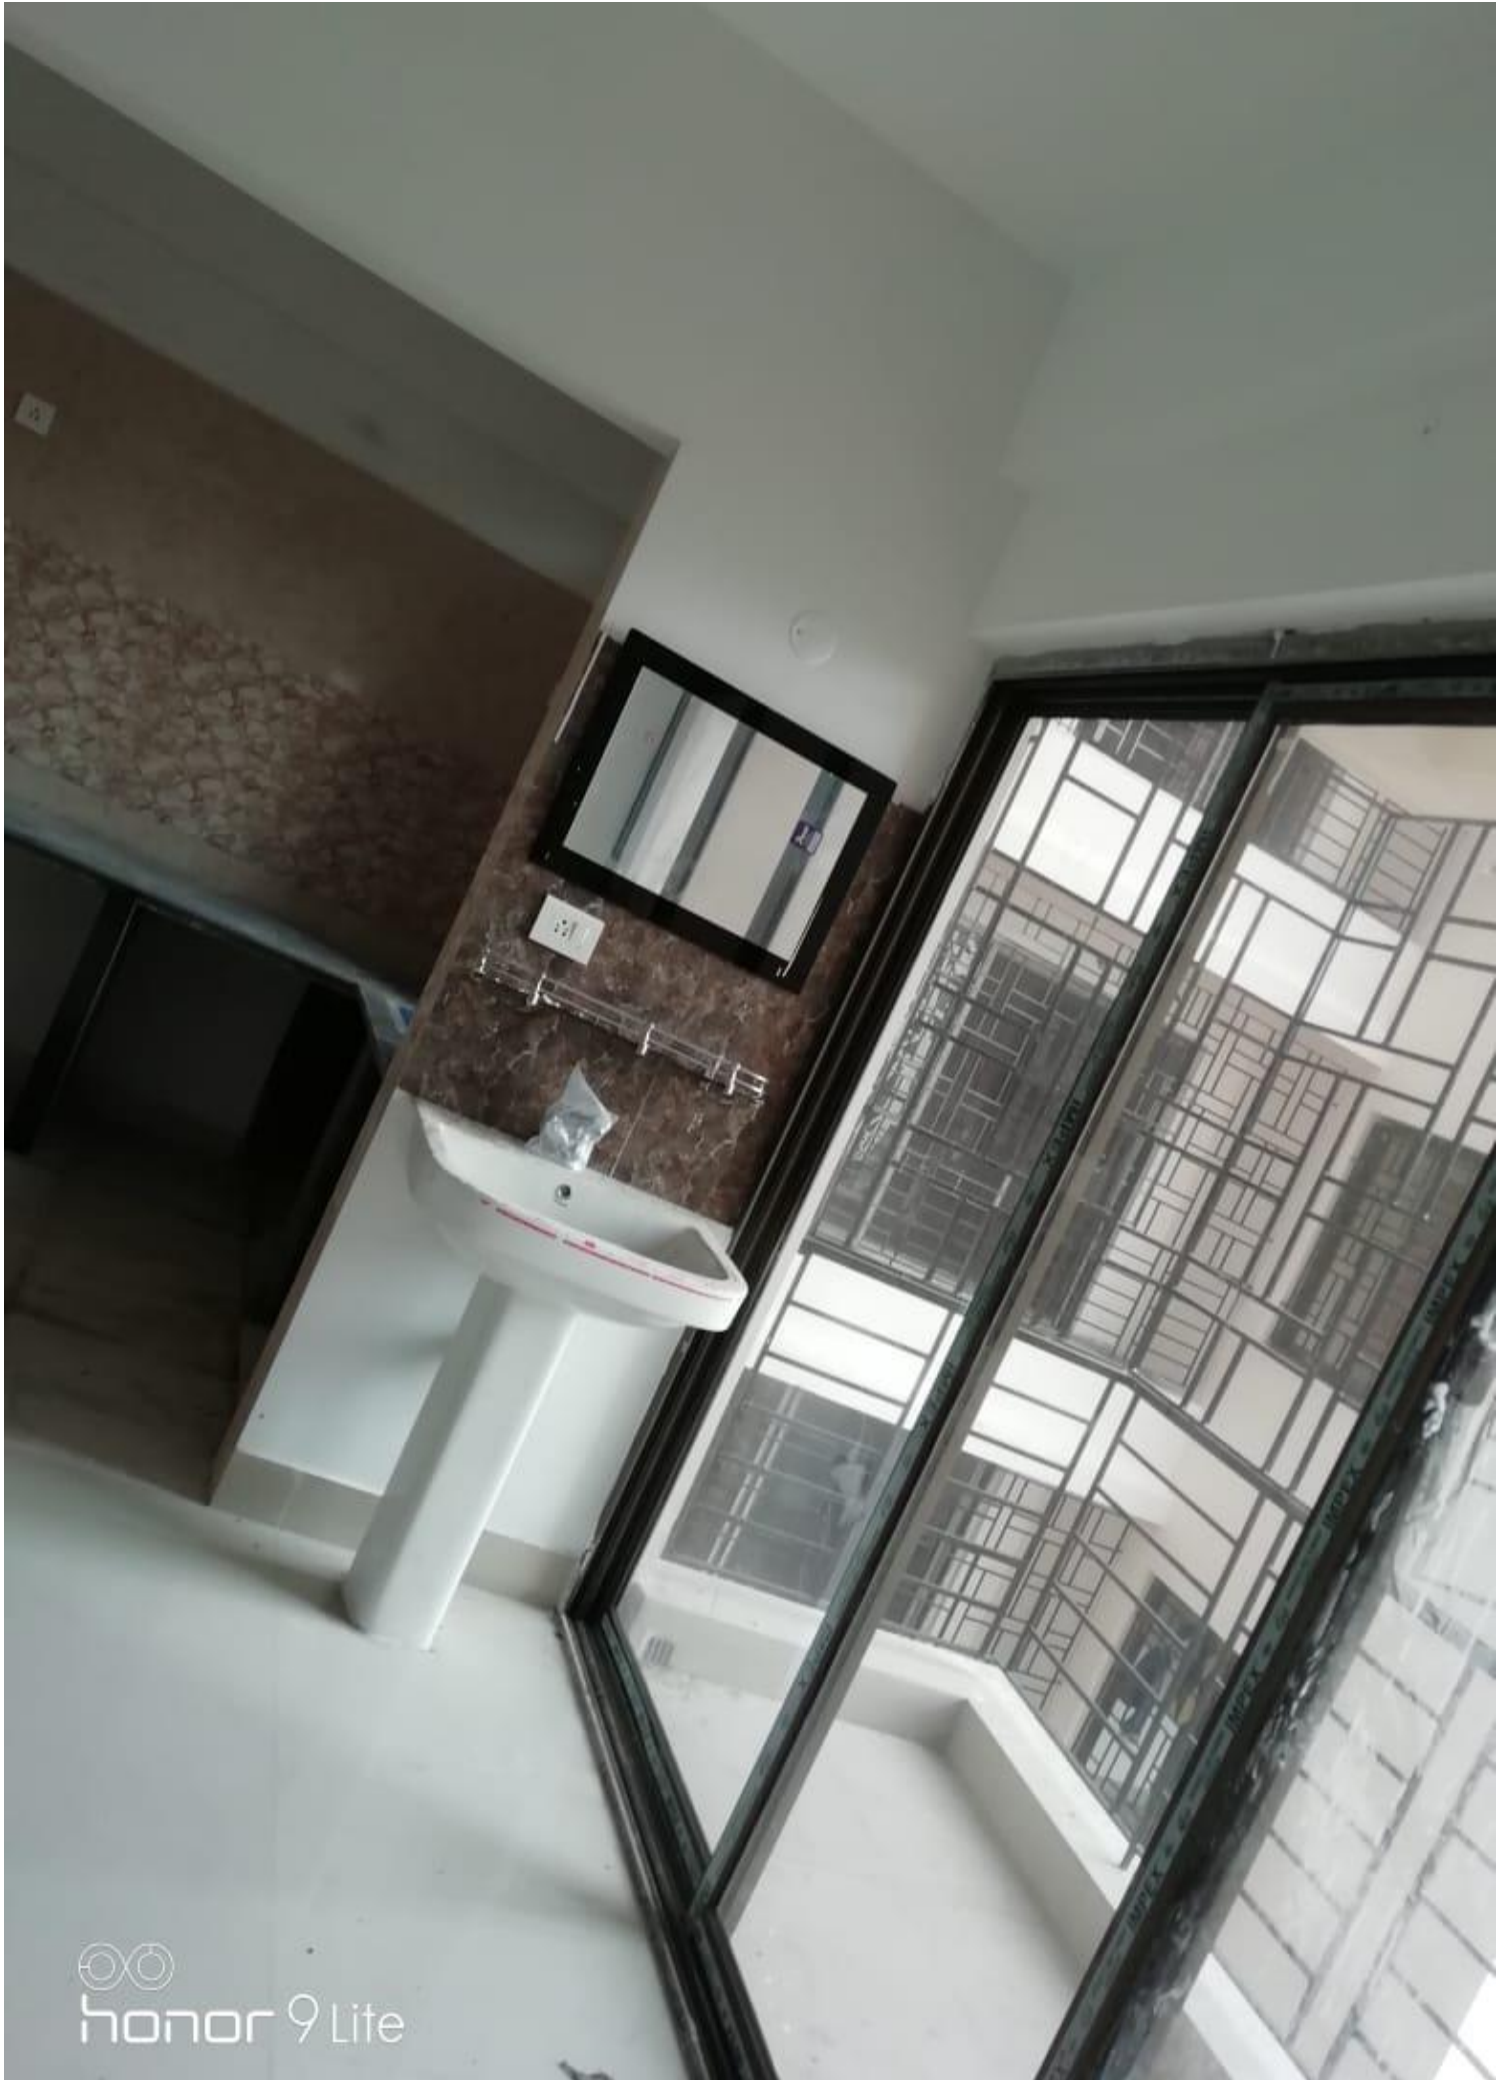

PREMIUM & ELEGANT



PREMIUM & ELEGANT



PREMIUM & ELEGANT



PREMIUM & ELEGANT



PREMIUM & ELEGANT




PREMIUM & ELEGANT



PREMIUM & ELEGANT



PREMIUM & ELEGANT

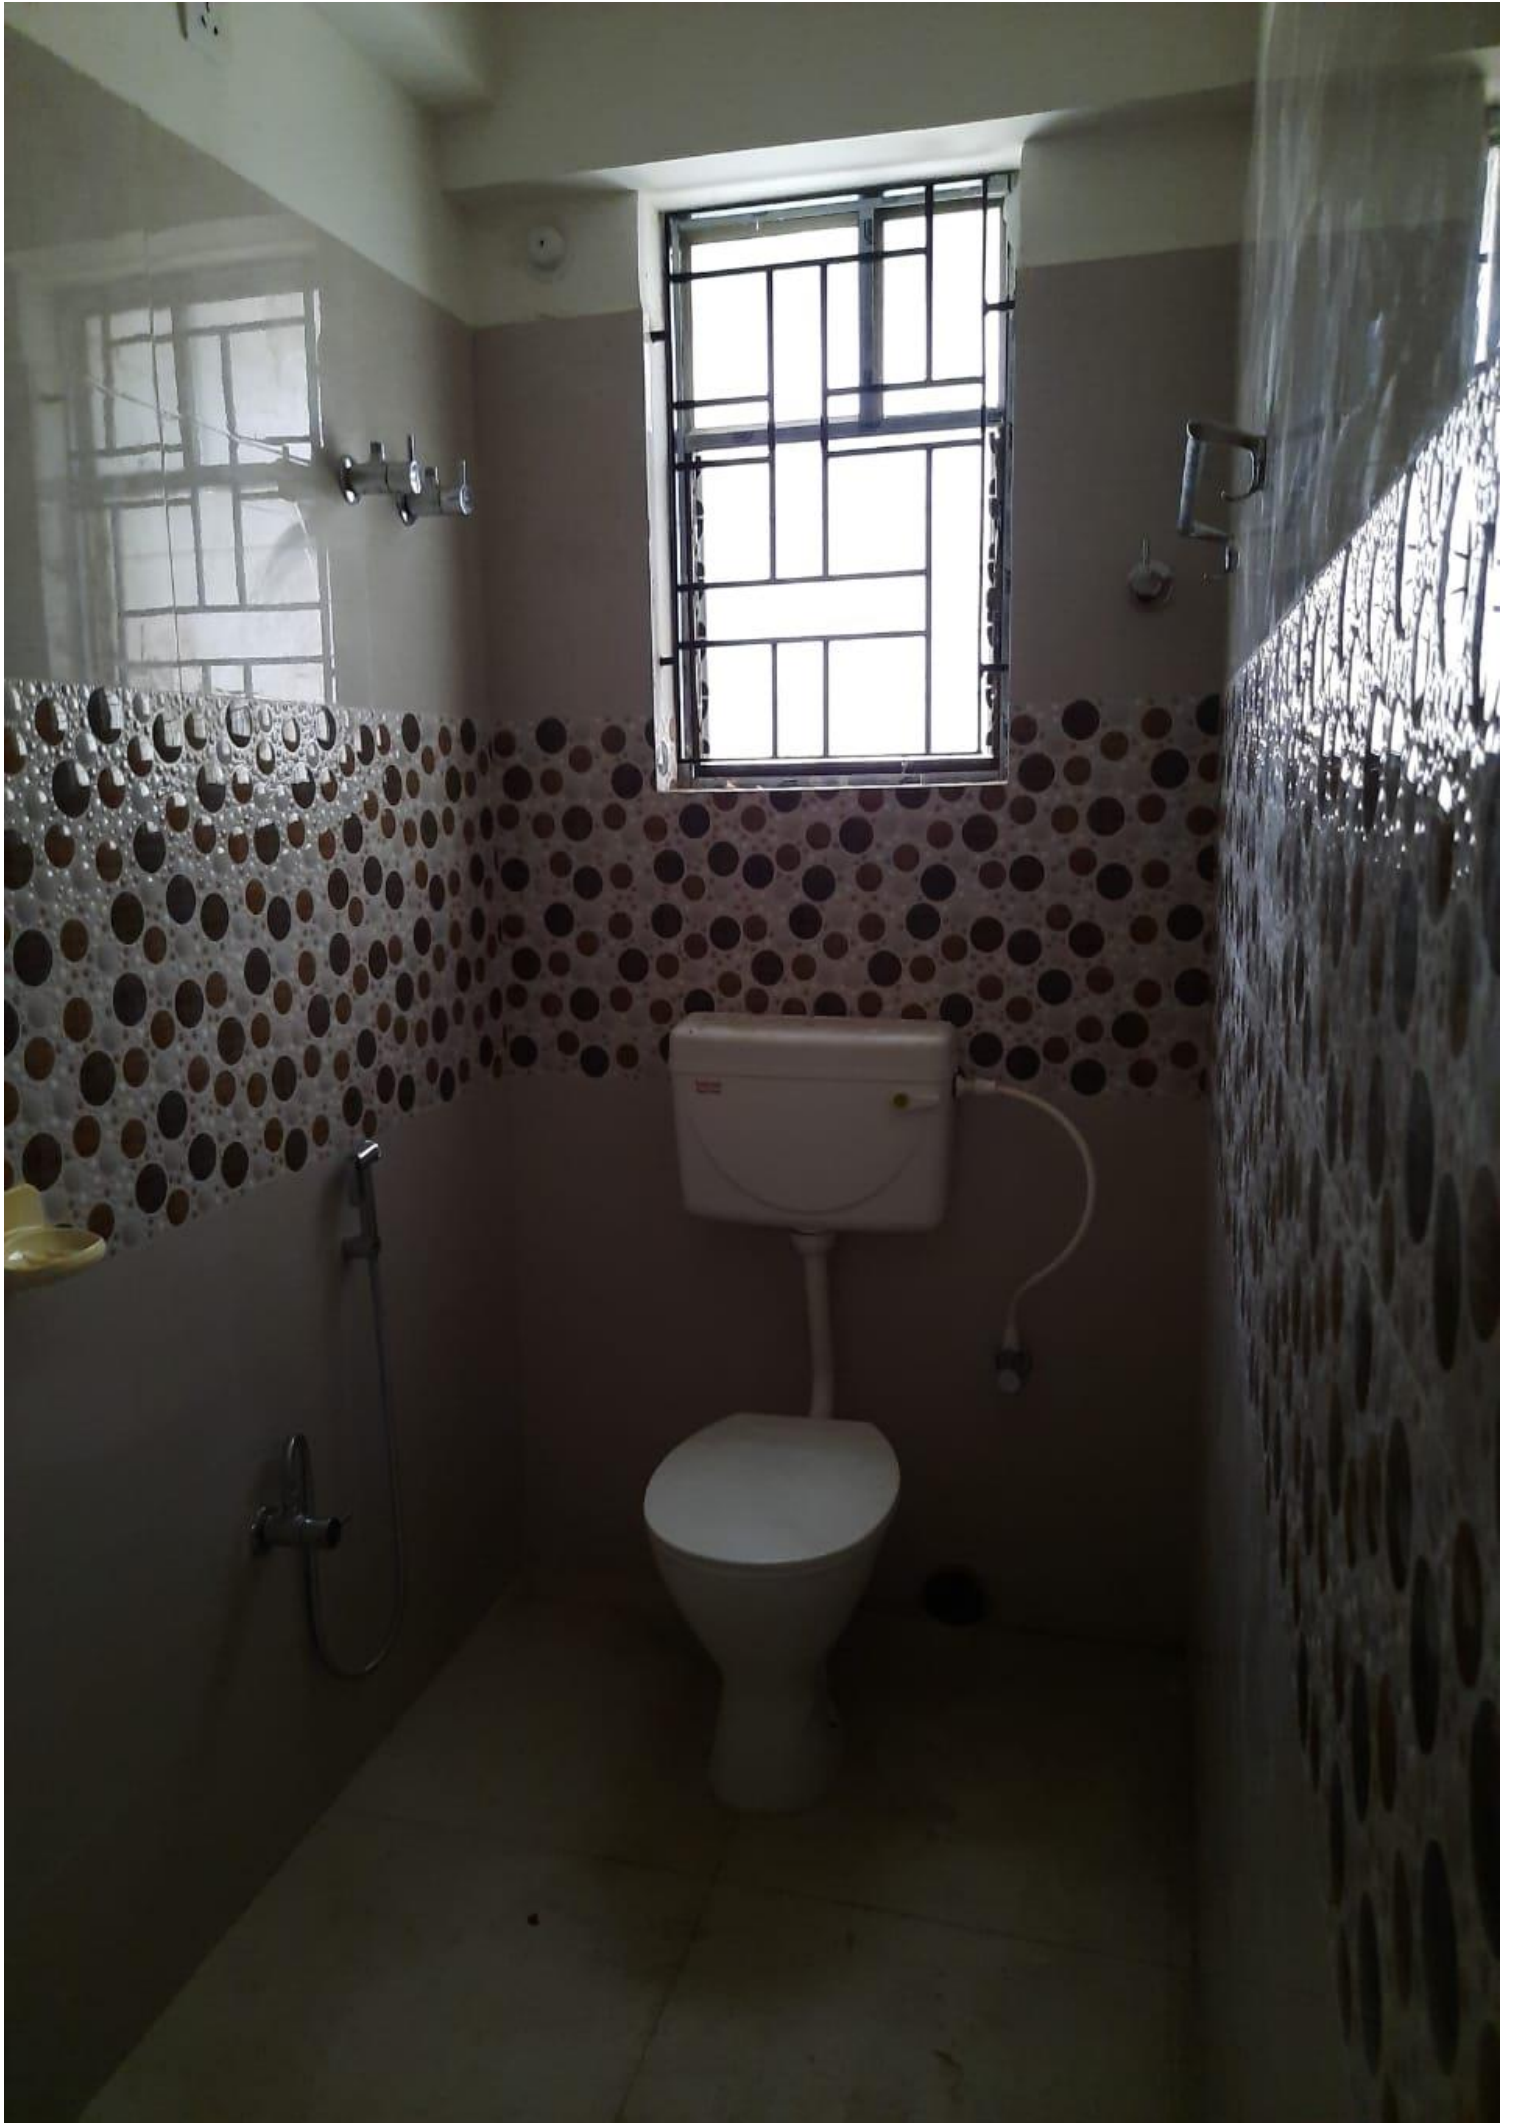

PREMIUM & ELEGANT



PREMIUM & ELEGANT



PREMIUM & ELEGANT



CLASSIC



CLASSIC



CLASSIC



CLASSIC



CLASSIC



CLASSIC



CLASSIC



CLASSIC




CLASSIC



CLASSIC



CLASSIC

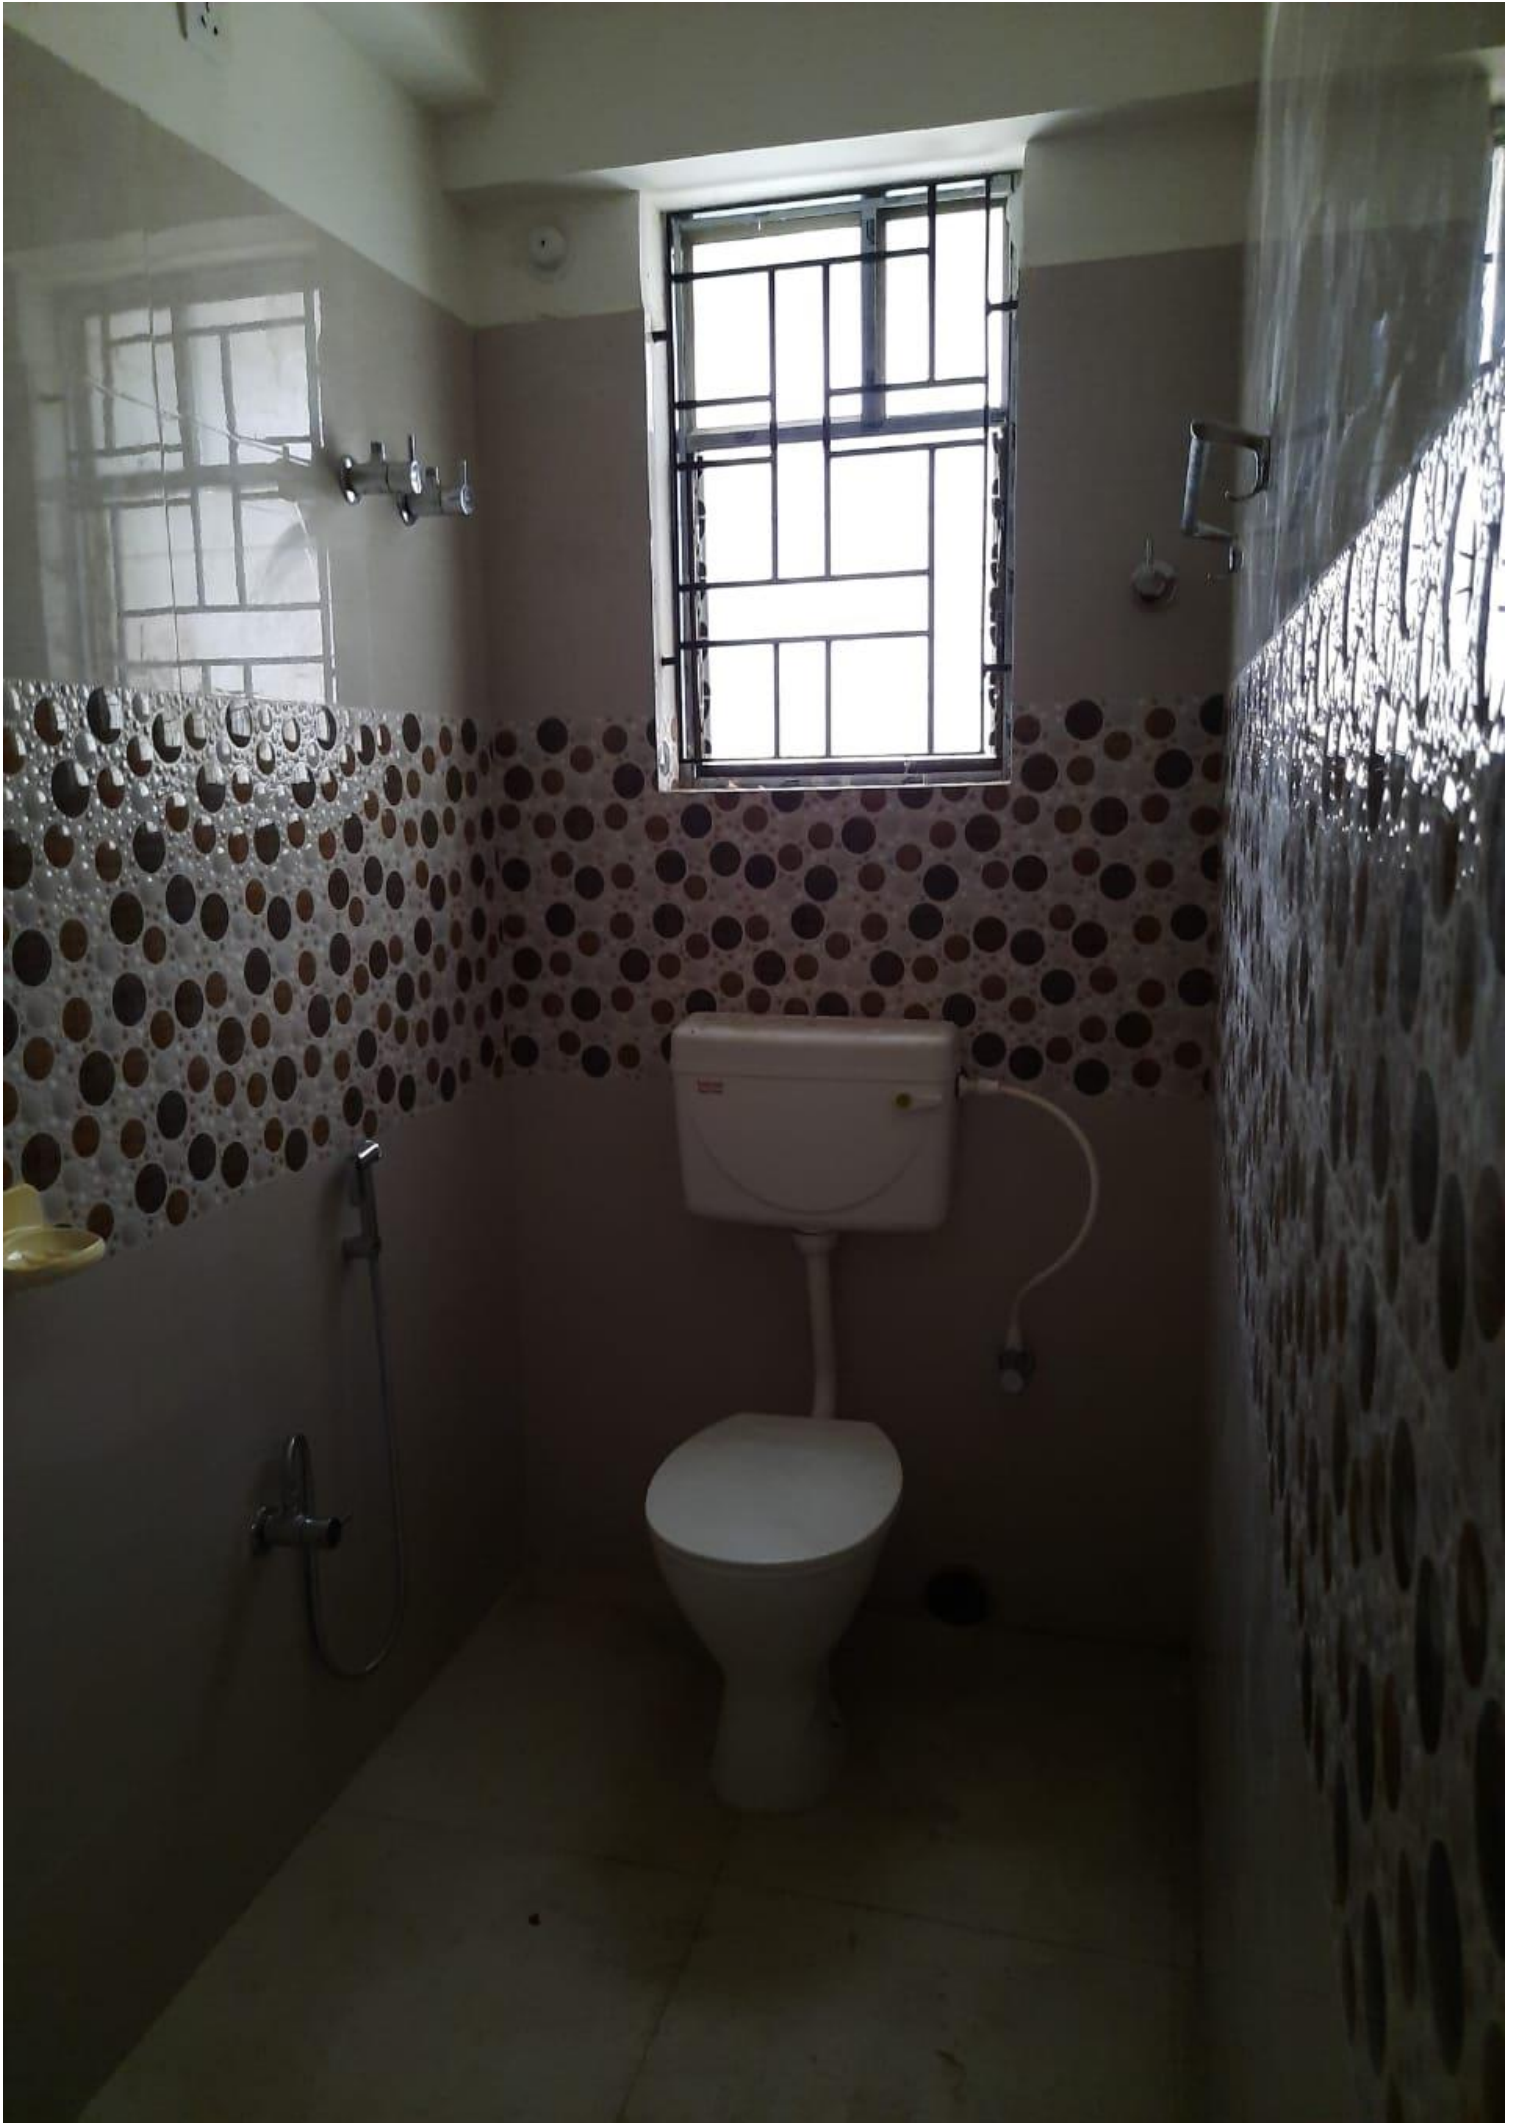

CLASSIC



CLASSIC



CLASSIC



CLASSIC



CLASSIC
