

MONTHLY PROGRESS REPORT OF AKANKSHA AT NEW TOWN AS STOOD ON 30/10/2017

SI No	Name of The Work	Name of The Agency	Estimated Amount	Tendered Amount	Date of Commencement	Date of Completion	% of The Physical Progress	Cumulative Physical Progress Achieved in (%)	Remarks
1	Construction of 3 (Three) nos.B type (Classic) G + 10 storied Residential Building including Structural and Plumbing and Electrical works Under AKANKSHASCHHEME at Rajarhat- Action Area-1D during the year 2015-16 (Tender no-12 of 2016-17 of S.E./S.C, Housing Directorate.)	Mackintosh Burn Limited	52,24,32,813/-	46,92,49,152/-	01/12/2016	30/11/2018	2.10%	29.00%	No. of column casted upto 3rd floor level Complete 1 st , 2 nd & 3 rd Floor Slab of Block B1 Casted. 1 st & 2 nd Floor Slab of Block B2 Casted. 1 st , 2 nd & 3 rd Floor slab of Block B3 Casted

Previous month Progress **26.90%**


MONTHLY PROGRESS REPORT OF AKANKSHA AT NEW TOWN AS STOOD ON 30/10/2017

S l N o	Name of The Work	Name of The Agency	Estimated Amount	Tendered Amount	Date of Commencement	Date of Completion	% of The Physical Progress	Cumulative Physical Progress Achieved in (%)	Remarks
2	Construction of 3 nos. (G+10) storied A1 type (Premium) and 1 no A2 type(Elegant) Residential Building, Community Hall and Sub-Station Building twonos. including main sewer line,underground supply system, Rainwater Harvesting Pit (3 nos.)Horticulture & BituminousRoad under AKANKSHA SCHEMEat Rajarhat Action Area 1D during the year 2015-16: Structural, S & P, Electrical andRoad Works(Tender no- 18 of2016-17 of S.E./S.C, Housing Directorate.)	Delta Construction	73,44,71,942/-	61,83,51,928/-	16/01/2017	15/01/2019	1.50%	23.00%	<p>No. of Piles completed = 910 out of 910</p> <p>No. of vertical Load test carried out =14 and integrity test = 170 nos</p> <p>No. of Pile Cap Completed = 160 out of 218 nos.</p> <p>1st Floor, 2nd, 3rd & 4th Floor roof Level slab casting of Premium-1. 1st & 2nd floor roof level slab casting of Premium 2 completed & 1st Floor roof level Slab Casting of Premium 3Completed, Earth Excavation work of Elegant Building is Started.</p>

Previous month Progress **21.50%**



PREMIUM 1 - 4th SLAB

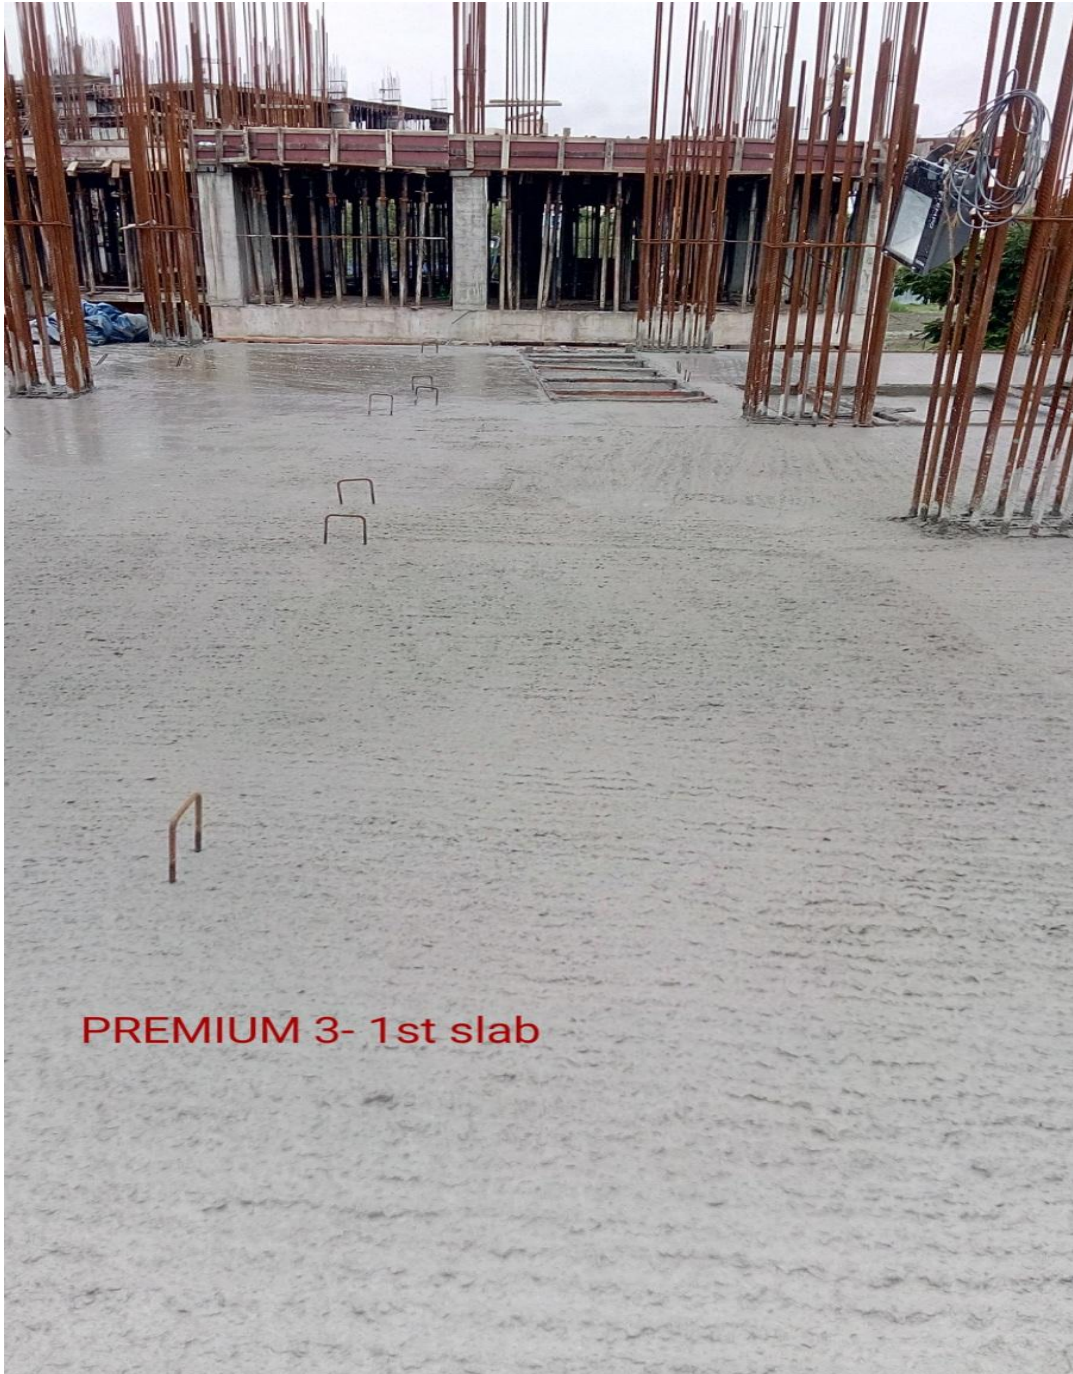

PREMIUM 3 – 1st SLAB



PREMIUM 2 – 2nd SLAB



ELEGANT earth work for PILE CAP



CLASSIC – 1



CLASSIC – 2



CLASSIC - 3
