

MONTHLY PROGRESS REPORT OF "AKANKSHA PROJECT" AT NEW TOWN AS STOOD ON 31-10-2018

Sl No	Name of The Work	Name of The Agency	Estimated Amount (Rs.)	Tender Amount (Rs.)	Date of Commencement	Date Of Completion	Physical Progress	Cumulative Physical Progress Achieved	Financial Progress	Remarks
1	Construction of 3 (Three) nos B type (Classic) G+10 storied Residential Building including Structural, Sanitary and Plumbing and Electrical works under AKANKHA Scheme at Rajarhat Action Area -1D during the year 2015-16. (Tender NO:- 12 of 2016-17 of SE/S.C, Housing Directorate)	Mackintosh Burn Limited	52,24,32,813.00	46,92,49,152.00	01/12/2016	30/11/2018	1.00%	60.50%	43.03%	<p>1. Classic-1 Building :- Casting up to Roof level Completed (G+10).</p> <p>2. Classic-2 Building :- Casting up to Roof level Completed (G+10).</p> <p>3. Classic-3 Building :- Casting up to Roof level Completed (G+10).</p> <p>Brick work:- Classic-1:- Upto 10th Floor Complete. Classic-2:- Upto 9th Floor Complete. Classic-3:- Upto 10th Floor Complete.</p> <p>Plaster Work:- Classic-1:- Upto 9th Floor Complete. Classic-2:- Upto 9th Floor Level Complete. Classic-3:- Upto 9th Floor Level Complete.</p>

Previous Month Progress:- 59.50%

MONTHLY PROGRESS REPORT OF "AKANKSHA PROJECT" AT NEW TOWN AS STOOD ON 31-10-2018

Sl No	Name of The Work	Name of The Agency	Estimated Amount (Rs.)	Tender Amount (Rs.)	Date of Commencement	Date Of Completion	Physical Progress	Cumulative Physical Progress Achieved	Financial Progress	Remarks
2	Construction of 3 (Three) nos (G+10) Storied A1 Type (Premium), One no (G+10) Storied A2 Type (Elegant) Residential Building, Community Hall and Substation Building [2 nos.] including Main Sewer Line, Under Ground water Supply System, Rainwater Harvesting pit, Rain water Recharge pit [3 Nos.], Horticulture & Bituminous Road under AKANKSHA Scheme at Rajarhat, New Town Action area-1D during the year 2015-16: Structural, S & P, Electrical and Roads works. (Tender No:-18 of 2016-17 of the S.E/S.C,Housing Directorate)	Delta Construction	73,44,71,942.00	61,83,51,928.00	16/01/2017	15/01/2019	1.10%	55.60%	43.57%	<p>1. Premium-1 Building :- Casting up to Roof level Completed (G+10).</p> <p>2. Premium-2 Building :- Casting up to Roof level Completed (G+10).</p> <p>3. Premium-3 Building :- Casting up to Roof level Completed (G+10).</p> <p>4. Elegant Building :- Casting of 9th Slab (G+8) Completed.</p> <p>5. Brick Work Premium:1 :-Upto 9th Floor Complete. Premium-2 :- Upto 9th Floor Complete. Premium-3:-Upto 9th Floor Complete. Elegant:-up to 4th Floor</p> <p>6.Plaster Work :- Premium-1:-Up to 9th Floor Complete. Premium-2 :- Upto 9th Floor Complete. Premium-3:- Upto 9th Floor Complete. Elegant:-up to 3rd Floor Complete.</p>

Previous Month Progress:-54.50%



CLASSIC BLOCK – 1



CLASSIC BLOCK – 1



CLASSIC BLOCK – 2



CLASSIC BLOCK – 2




CLASSIC BLOCK – 3



CLASSIC BLOCK – 3




PREMIUM 1 – ROOF SLAB COMPLETED

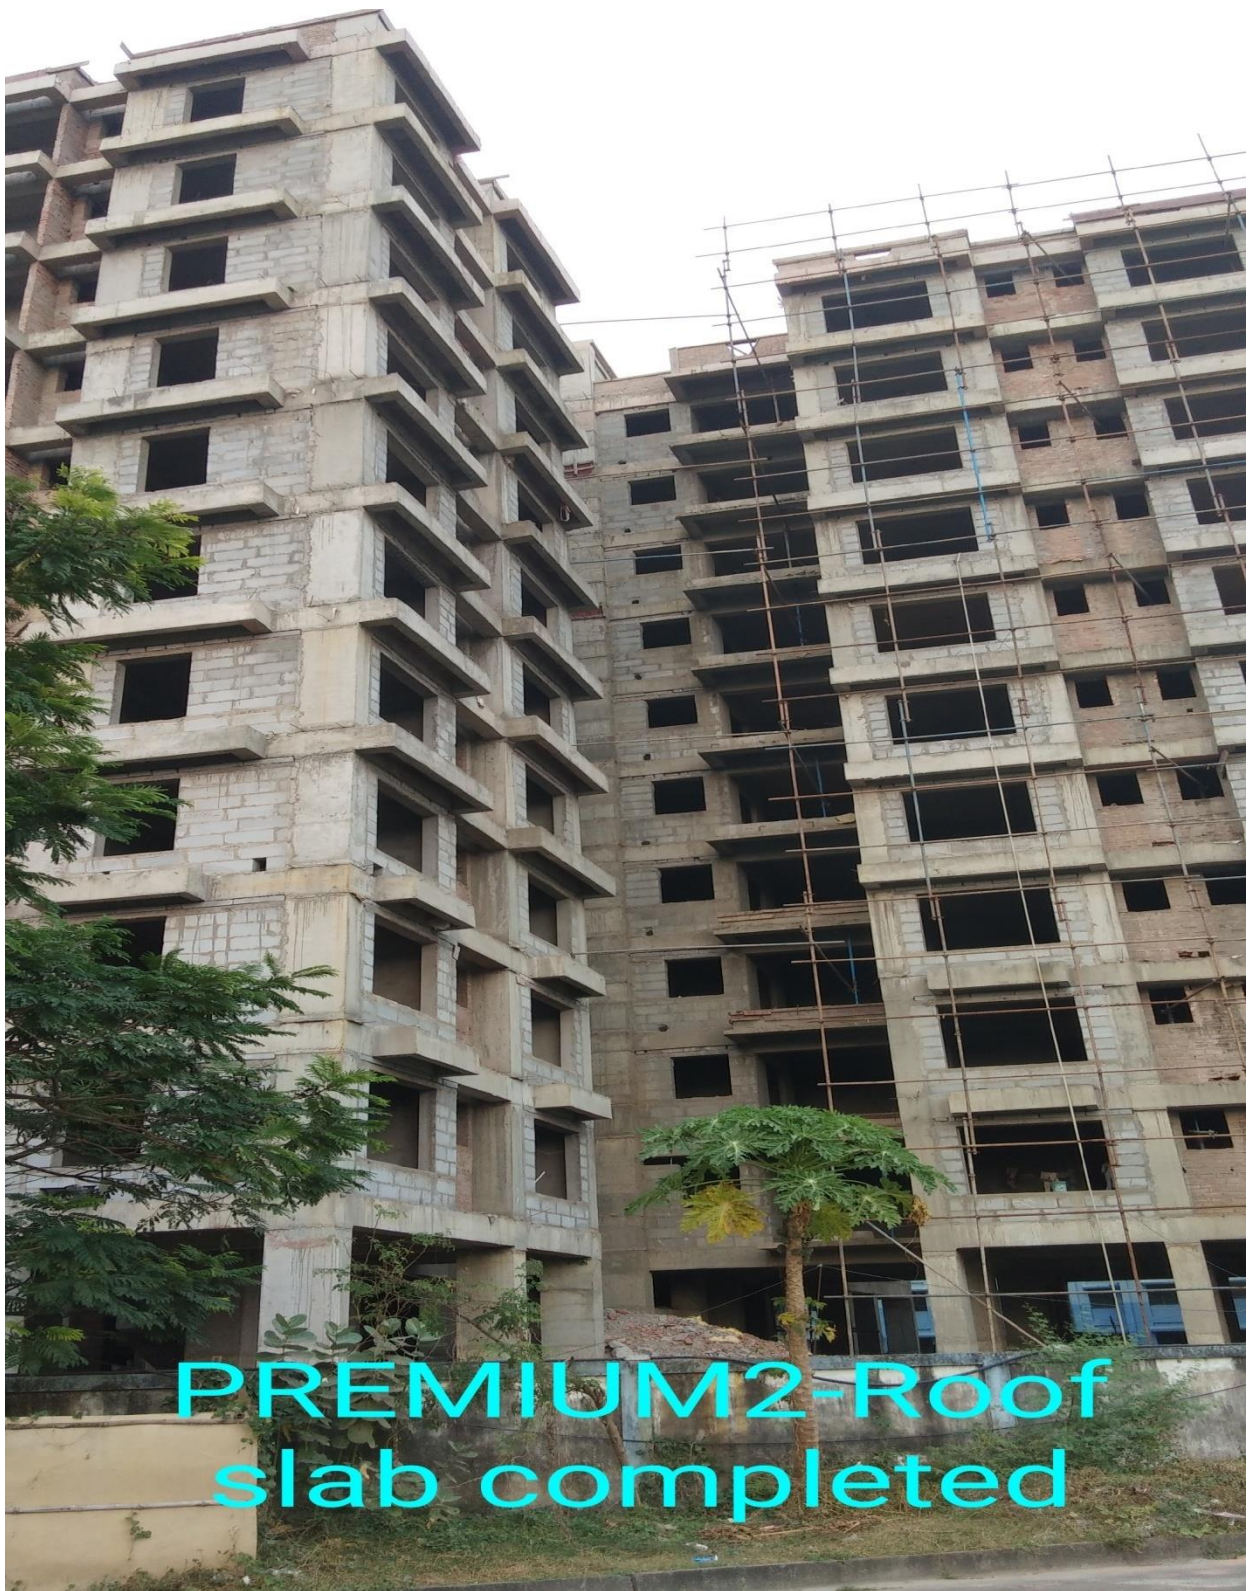

PREMIUM – 2 – ROOF SLAB COMPLETED



PREMIUM – 3 – ROOF SLAB COMPLETED

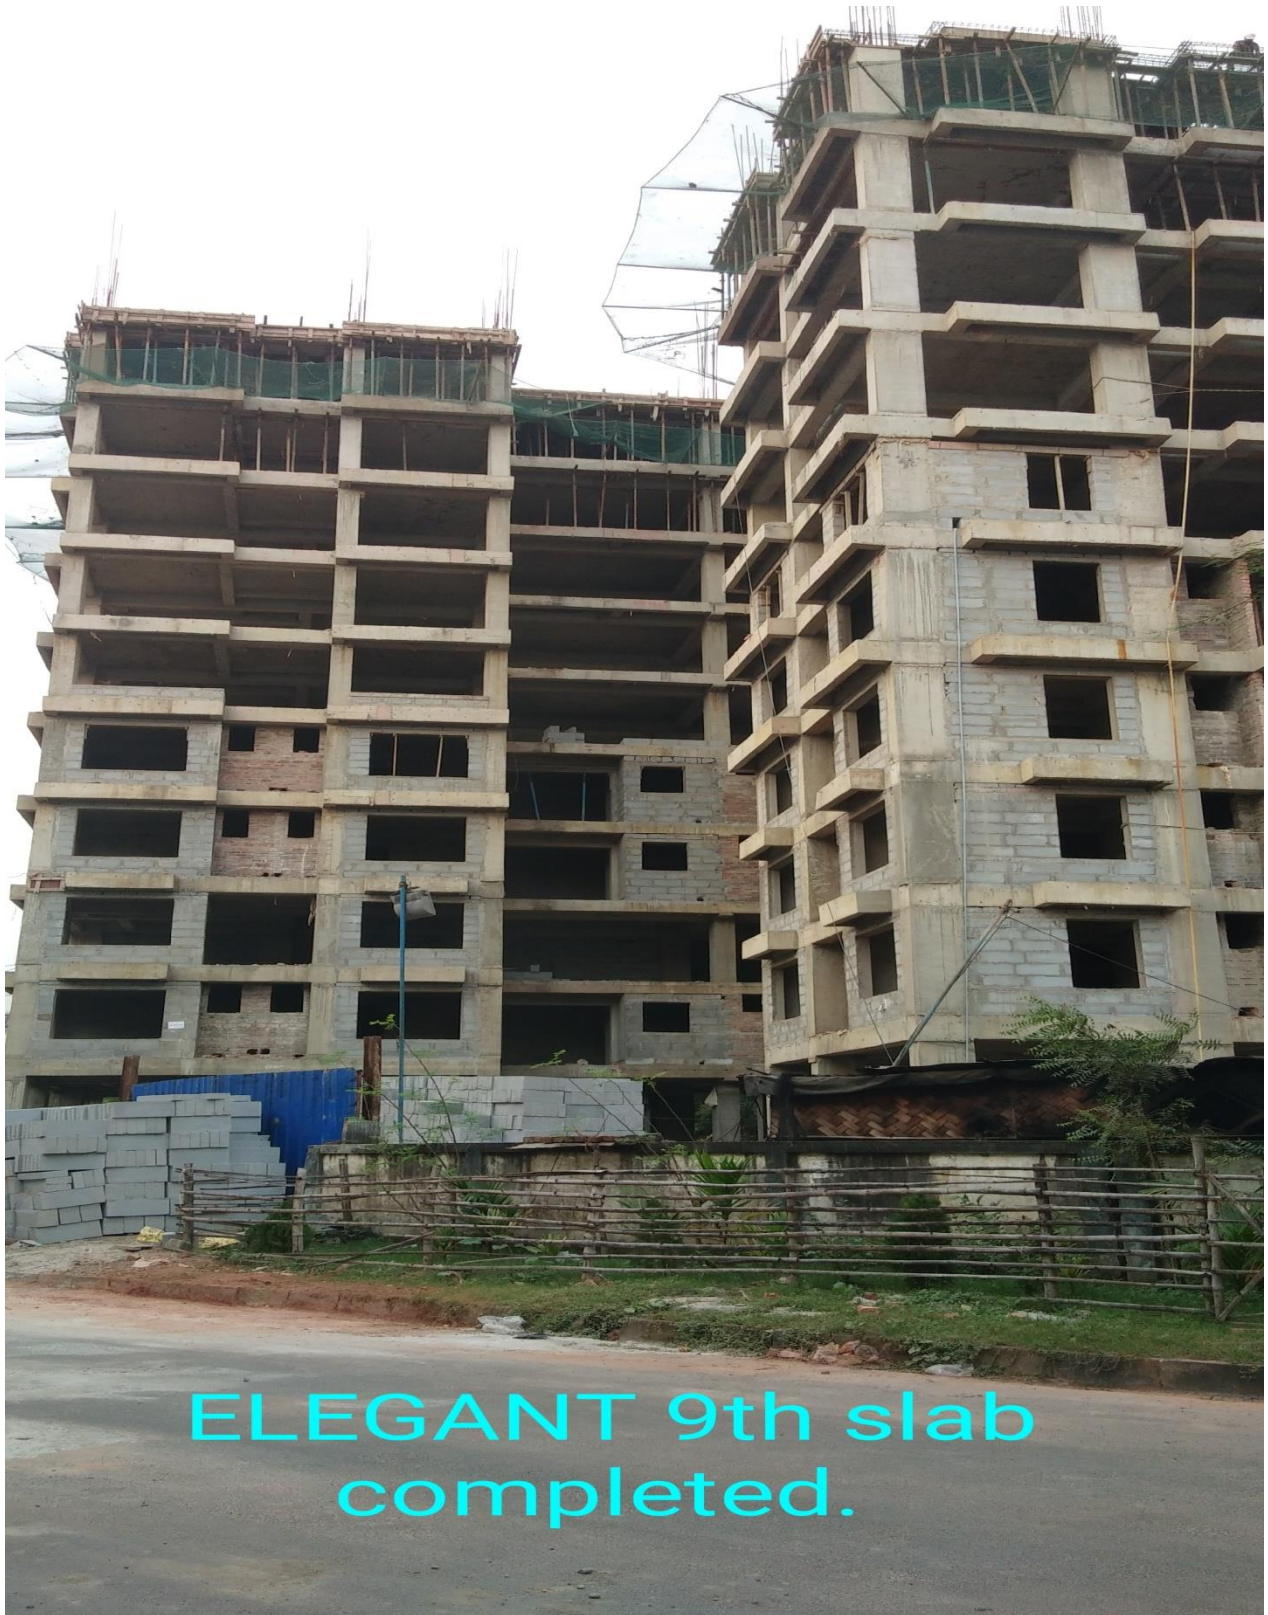

**ELEGANT 9th slab
completed.**

ELEGANT 9TH SLAB COMPLETED
